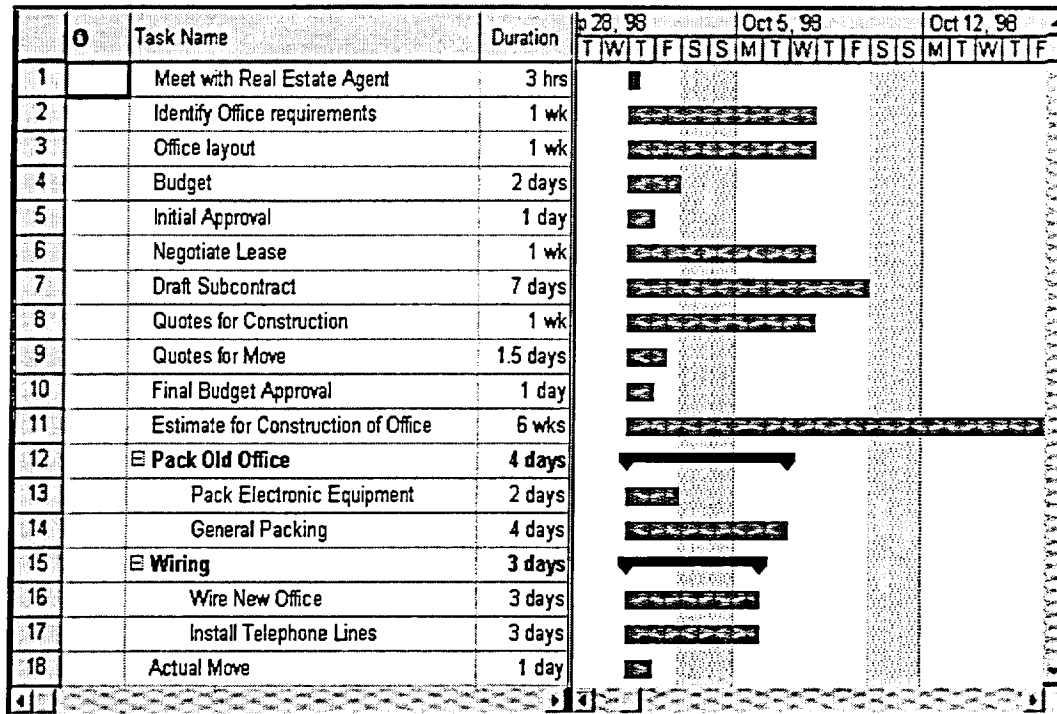


14. Save the project as **H:\Doc\Move-Rev 2a.mpp**. Your project should look similar to **Figure 2-11**.



**Figure 2-11: The Project After Saving**

15. Link all the tasks in the project.
16. The *Quotes for Move* task is not truly dependent on *Quotes for Construction* but rather on *Initial Approval*. Make the necessary changes.
17. The summary task *Wiring* is not dependent on the summary task *Pack Old Office*. Rather, it is dependent on the completion of *Estimate for Construction of Office*. Make the necessary changes.
18. *Final Budget Approval* is not only dependent on *Quotes for Move* but is also dependent on *Quotes for Construction*. Make the necessary changes.
19. Edit the task *Estimate for Construction of Office* to read **Construction of Office**.
20. The tasks *Install Telephone Lines* and *Wire New Office* must finish at the same time. Make the necessary dependency change.
