		Task Name	Duration
1		Meet Real Estate Agent	3 hrs
2		Office Needs	1 wk
3		Identify Office Needs	1 wk
4		Budget	2 days
5		Initial Approval	1 day
6		Negotiate Lease	1 wk
7		Draft Subcontract	7 days
8		Final Budget Approval	1 day
9		Estimate for Construction	6 wks
10		Quotes for Construction	1 wk
11		Quotes for Move	1.5 days
12		Pack Equipment	2 days
13		General Packing	4 days
14		Actual Move	1 day
15		Unpack	3 days
16		New Office Party	3 hrs
17		End Move	0 days

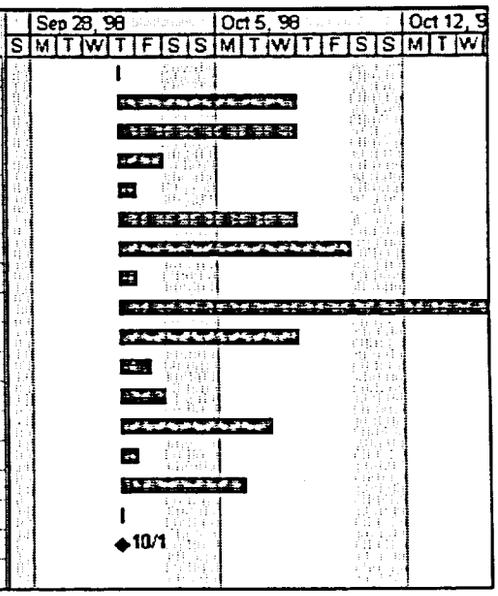

Figure 1-12: The Final Project

12. In the chart pane, move to the end of the project.

13. In the chart pane, move to the beginning of the project.

14. Close the project file.
